



Daily Log: Wednesday 7/2/2025



Daily Log Completed

The Daily Log was completed by Ray Hutsel on Wed, Jul 2, 2025 at 12:52 PM CDT.

VISITOR LOG

No.	Visitor	Start Time	End Time	Comments
1		09:45 AM	09:45 AM	None, while onsite.

NOTES LOG

No.	Issue?	Location	Comments
1	No	Early Childhood Center	Rubblestone Wall Tuckpointing (Tremco) -Staat continues to grout at the west end. Area A. -Staat continues to remove existing grout and loose stones. Advancing east to Area B. Concrete Replacement (Tremco) -Cleanup and removal of new concrete stains still needed. -Recaulk where the concrete work removed existing. Asphalt Paving (Tremco) -Layout complete.
2	No	Elementary School	Concrete Work (Tremco) -Cleanup of new concrete work stains still needed. Asphalt Paving (Tremco) -Underground drain pipes installed and backfilled. It was noted to Steve that the actual installed piping is not per the contract and proposal. It is NAVIGATE's position that a credit is due. -Contract required concrete removal in two locations not done. A credit is due. Milling of the existing asphalt pavement has started.
3	No	Middle School & High School Projects	Field & Track Projects (Byrne & Jones) -Concrete work is complete. -Field work is underway with stripping and removing the sod. Tuckpointing (Tremco) -Tuckpointing of the west wall continues. Concrete Replacement (Tremco) -Cleanup of the new concrete splatters/spills is needed. -Review of the Maintenance Drive curb vs. retaining wall continues. -The permanent fiber cable repair is scheduled by 7/13. -The MSHS concrete replacement at the two ADA spaces is on hold awaiting a drawing from Frontenac Engineering. Ceiling Tile Replacment (Friend) -The base contract removal and replacement work is complete. -Need to meet with Scott to review the two stairwells.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
65°F	85°F	72°F	0.00 in.	0.00 in.	0.06 in.	44%	76%	94%	64°F	1.9 mph	5 mph	4 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Clear 66°F	Partly Cloudy 78°F	Partly Cloudy 86°F	Partly Cloudy 90°F	Partly Cloudy 88°F	Clear 81°F

OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea	Calamity
1	09:45:00 AM	No							
Comments:									

PHOTOS



[15D0112E-5379-4C5D-8BA7-E9B5B8FC9A48.jpeg](#)

MSHS - Survey layout at the ADA parking spaces complete.



[B399422B-7ACA-4020-8C66-4CBBF3578642.jpeg](#)

MSHS - Basketball Court concrete complete.



[B493A815-6C58-458E-9DE2-F1B9E4C2CF1F.jpeg](#)

MSHS - Field grading as of about Noon today.



[E4B7EA40-D851-4136-A42E-B6305F3E1AC1.jpeg](#)

MSHS - Exising sod stockpile.



[7FA37A64-FBAB-49B9-9FB1-A879C2A0F378.jpeg](#)

MSHS - Loading out from the spoils pile.



[8622175A-2A5D-4B34-B7BA-E07C4494D13D.jpeg](#)

MSHS - New ceiling tiles at 4th Floor




[7B51A112-83D2-4D43-BAD6-C37168DA7F3C.jpeg](#)

MSHS - New ceilings at 4th Floor



[A22A96D5-6643-4EA2-9193-7D85D6D316F5.jpeg](#)

MSHS - New ceilings at 4th Floor east.

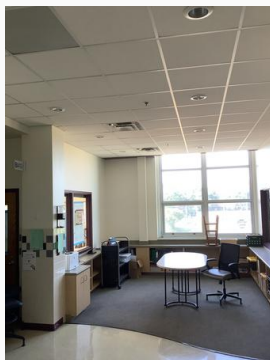

[80A0FC21-CD28-481F-9EEC-99C660CBB410.jpeg](#)

MSHS - New ceilings outside B410.




[F1563FF0-D9CB-49B1-A05C-CE5977FC0354.jpeg](#)

MSHS - New ceilings at Corridor 4R.



[66FF87AE-5854-49CC-9B7F-AC3390ECD161.jpeg](#)

MSHS - Review replacment of ceiling tiles at the Stairs with Freind.

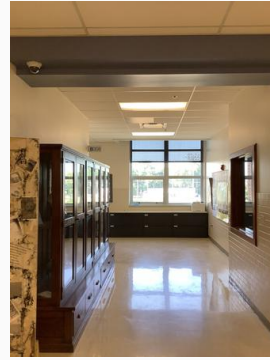

[BD3F5882-8648-4048-A7F7-B43EC3C7259D.jpeg](#)

MSHS - New ceilings at the 3rd Floor corridor.



[359106BA-088E-40C9-B247-DD01FDCECD9D.jpeg](#)

MSHS - New ceilings at Corridor 4R.



[EE7BFE1D-6E86-4B1C-90F0-DBFA9DF8EC9A.jpeg](#)

MSHS - New ceilings at 3rd Floor Corridor.



[319EFB20-54DE-4584-8030-2EE082BA8041.jpeg](#)

MSHS - New ceiling tiles at 2nd Floor Corridor.



[CDE00404-7804-4ED8-8ADB-D2B86F605366.jpeg](#)

MSHS - Tiles replaced and waxing this 2nd Floor corridor.




[37027D61-2594-4D8F-863B-D97DF06BA383.jpeg](#)

MSHS - 1st Floor Corridor new ceiling tiles installed.



[B735B8C5-D38C-4261-A5FF-45617F432DAC.jpeg](#)

MSHS - Tech Electronics/Kaemmelen Electric have mobilized and started the Camera Work.

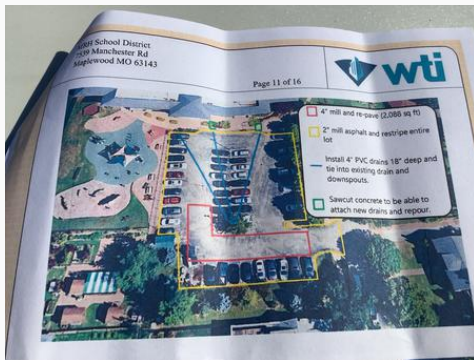

[B3A38FED-153B-46C7-B652-41F245BA53AC.jpeg](#)

Tremco/WTI contract drawing for the Elementary School Parking Lot work.



[68D2BB48-91C4-4C3F-9332-CEE4A0B3C5D8.jpeg](#)

ELEM - Stockpiled concrete parking bumpers.



[2F13FB56-74AC-46A7-9F06-7DC4D2E737FB.jpeg](#)

ELEM - Underground storm piping not the same as the contract drawing.



[56DAE12D-8C91-4287-8F77-6504B44D8EA9.jpeg](#)

ELEM - Milling of the existing asphalt.



[62CAEB60-BAD0-4048-9E1E-690C1D60F213.jpeg](#)

MSHS - Entrance/ADA concrete placement on hold for drawing.




[3AA5CC20-E358-4C13-9EF0-4C26F03597C6.jpeg](#)

MSHS - Friend dumpster full of removed ceiling tiles.



[7155B9E8-E395-4CB8-B48D-8565A1A1007B.jpeg](#)

MSHS - New Fiber Optic cable to be installed 7/10 & 7/11. Concrete curb still under review.

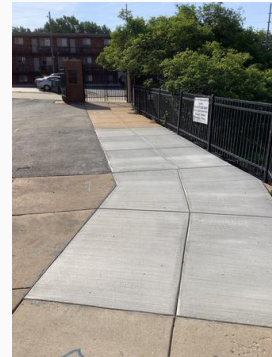

[7F5175E0-DB71-4B34-9CAA-F9545D497AEB.jpeg](#)

MSHS - Cleanup needed at new concrete area.



[346FCC8F-EF4E-4526-8A43-2E9BB6BD962B.jpeg](#)

MSHS - Tuckpointing at the west wall continues.



[697C7C37-61D9-4E1E-9B01-4C63A75747EA.jpeg](#)

MSHS - Early morning view of the field grading work progress.



[9083C803-3EFF-4E2B-B67E-1CBA389FAF21.jpeg](#)

ELEM - Cleanup at the new concrete area still needed.




[E391158F-F417-4115-82D3-915DC97ADE16.jpeg](#)

ECC - Underground pipe leak needs fixing.



[5B0EE51B-50E6-48F8-859C-D2413BE95901.jpeg](#)

ECC - Removal of existing grout at the rubblestone wall continues.

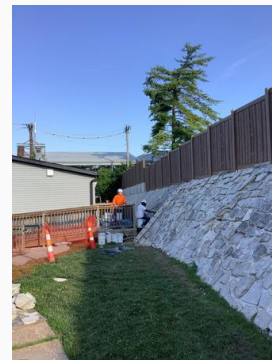

[475A3AA1-061F-474A-9C23-5505A05692A4.jpeg](#)

ECC - Grouting continues at the west end of the rubblestone wall.



[07C2402A-6F80-4D5B-B16E-3EA1FA682AD5.jpeg](#)

ECC - Concrete cleanup still needed at the replacement concrete area.



[006D2BA7-5ADB-4791-98D2-17CC88EC5E63.jpeg](#)

ECC - Cleanup and caulk repair needed here.
