



Daily Log: Wednesday 7/16/2025



Daily Log Completed

The Daily Log was completed by Ray Hutsel on Fri, Jul 18, 2025 at 01:23 PM CDT.

VISITOR LOG

No.	Visitor	Start Time	End Time	Comments
1		12:23 PM	12:23 PM	Michael onsite with the Bryne & Jones team for the bi-weekly construction progress review. See separate NAVIGATE Meeting Notes for this meeting.

NOTES LOG

No.	Issue?	Location	Comments
1	No	Early Childhood Center	Tuckpointing (Tremco/WTI/Staat) -Grouting continues to the east. Area A about complete. -Removal of the existing grout and loose stones continues ahead in Area A. -WTI reports about 47% complete overall. Paving (Tremco/WTId/Keely) -The asphalt milling and replacement in complete in the lower lot and upper lot along with new asphalt curbs along the east north side of both areas. -Need to review a couple of questionable asphalt curbs areas at the upper lot. See photos.
2	No	Middle School & High School Projects	Tuckpointing (Tremco/WTI/Staat) -Tuckpointing continues on the Concession Stand/Storage building. -Completing brick infill work at the removed Main Gym window. Asphalt Paving (Tremco/WTI/Keely) -Completing the asphalt paving work at the small lot east of Martini. Concrete Work (Tremco/WTI/Gleeson) -Maintenance Drive temporary fiber cable still in place. Acceptance of the concrete curb vs. concrete retaining wall still to be resolved? -MSHS Existing ADA Concrete Work - Meeting held on Monday to review the Frontenac drawing. Camera Work (Tech Electronics) -Installation of the new cameras continues. Gym Ceiling Repairs (Legacy Construction) -Work is complete. See Legacy email with before and after pictures.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
73°F	94°F	82°F	0.00 in.	0.00 in.	0.00 in.	48%	74%	96%	72°F	6.1 mph	17 mph	32 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Partly Cloudy 74°F	Clear 82°F	Partly Cloudy 91°F	Partly Cloudy 95°F	Partly Cloudy 82°F	Partly Cloudy 80°F

OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea	Calamity
1	12:20:00 PM	No							
Comments:									

PHOTOS



[859CE1B0-D0BA-4ED1-A8BA-6D7AD1976D1A.jpeg](#)

MSHS - Kaemmerlen electrician installing cameras on the 1st Floor.



[15C7DD45-AFB4-4DFF-A9E6-AF3C61492C28.jpeg](#)

MSHS - Inside view of the Gym window brick up.



[E3A338F8-0B78-404F-9411-7F967DC6E99C.jpeg](#)

MSHS - MRH crews continue to make the floors shine! The new ceiling tiles look very nice too.



[A8B89752-0A05-40A5-9005-B5E9367D356D.jpeg](#)

MSHS - Pro Outdoor onsite installing the new field sprinkler systems.



[0060B6E6-835A-4A36-9FF0-7E54D8A0A286.jpeg](#)

MSHS - Collins & Herrman have marked the new underground borings for the new Daktronics scoreboard.



[B4FB7C9A-E452-4E6A-AEC0-05013AD0ED14.jpeg](#)

MSHS - New irrigation lines and control cable being installed at the west end of the field.



[A50C54F8-AF8C-4B26-B049-6C97E817B341.jpeg](#)

MSHS - View from the west end of the field.



[062CBE68-1367-47EB-9E35-CEB924160A77.jpeg](#)

MSHS - View from the southeast corner of the field. New drainage pipe/rock in place.



[BE2F0C8F-8F7E-420B-917C-9B3E54DA02C1.jpeg](#)

MSHS - Basketball court area has been backfilled.



[4FCE9D0C-1F01-4968-9B8A-469F86CC180D.jpeg](#)

MSHS - The north field new drain line is installed. Existing track surface also being removed.



[384FF0F8-AD87-4A68-A2A7-7C0A3C96E6ED.jpeg](#)

MSHS - Brick infill work at the Main Gym window.



[012ED896-437C-4C89-B5E1-9A161D15836D.jpeg](#)

MSHS - Tuckpointing going on at the Concession Stand building.



[6363EF10-B68A-4B45-9537-A20D21D95EE8.jpeg](#)

MSHS- Paving the small lot across Martinni.




[ED2851B0-8B92-4FCA-BD82-2FF6DF34F866.jpeg](#)

MSHS - Temporary fiber still in place.



[3BBD6675-CD3C-4E8B-8818-5610B33EDE95.jpeg](#)

MSHS - View from the Javelin runway

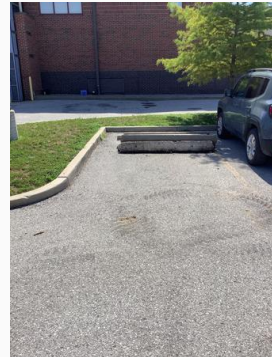

[ACAFEC13-1D46-4202-BC7F-9588BC940F3A.jpeg](#)

ECC - Where do these stored parking bumpers go?



[8BDFEA11-A058-4008-A486-08296C217413.jpeg](#)

ECC - Grout and loose stone removal continues.



[FB6FF574-F95C-4E4E-BEC0-7CE016D6AE95.jpeg](#)

ECC - Grouting in Area A about complete.



[1B62C672-F0DE-436A-9324-BEA4E2AB6BBD.jpeg](#)

ECC - Questional curb work?



[8A102FB0-D745-435B-B016-8089D4E40353.jpeg](#)

ECC - Questionable curb work?



[760A19D3-9AA2-4BC0-AB80-43BF1036FF10.jpeg](#)

ECC - Asphalt complete at upper level.



[4DE2AFB1-522F-4678-AAD5-13E86D544951.jpeg](#)

ECC - Overlay complete at the lower lot.



[C168322E-32D1-4974-899A-AA4C6172CB2F.jpeg](#)

ECC - View from main entrance of the lower lot.

By

Date

Copies To
